



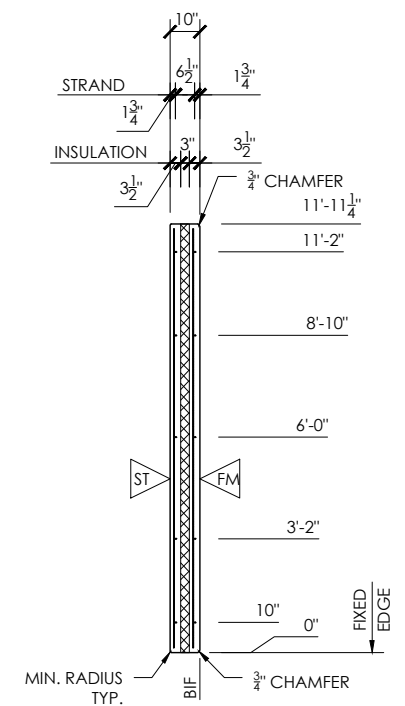

DIAGONAL = $46' - 5\frac{11}{16}"$

SYMBOLS
S.I.F. = SIDE IN FORM
B.I.F. = BOTTOM IN FORM
T.I.F. = TOP IN FORM
 **= STEEL TROWEL**
 **= FORM FINISH**

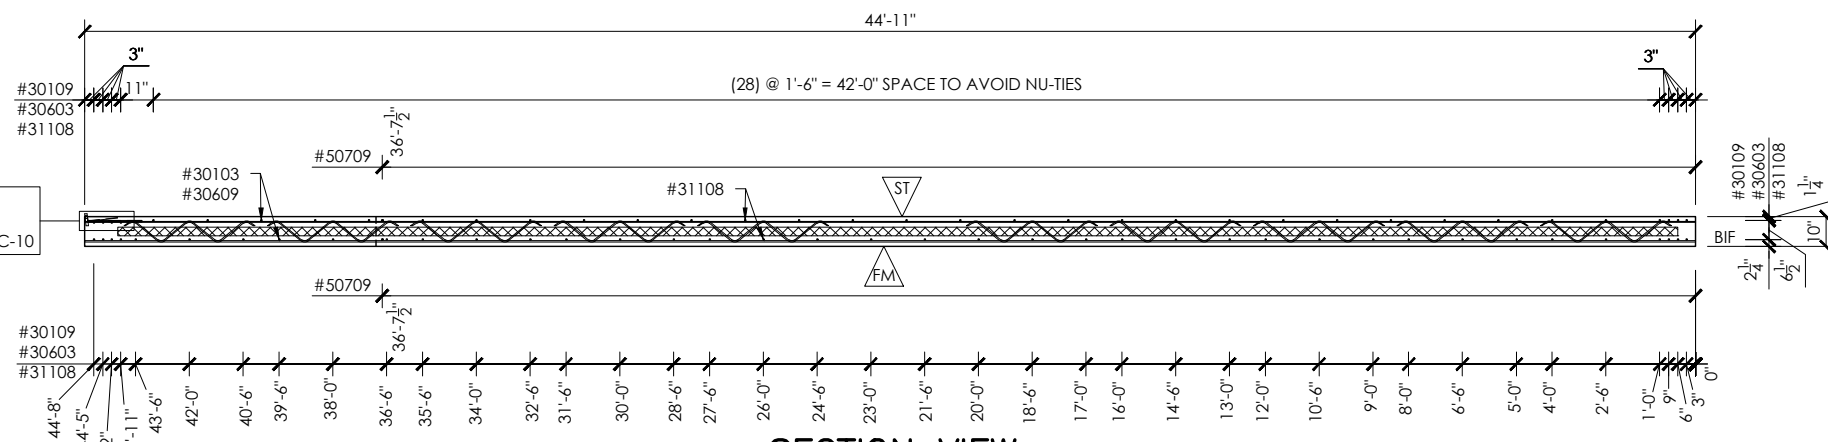

PRODUCTION NOTE:
UPPER #30103 & #30609
TIED BELOW STRAND @ PC-10

MINI-V		JVI-MINI-V (J FINISH)		1	EA
CI-63	3/4" DIA. x 3 1/2" CI-634312P COIL INSERT			2	EA
NU-TIE	7" NU-TIE			42	EA
PC-10	PL 3/4" x 4" x 0'-7" w/ (2) #4 X 1'-6" BAR & STEEL CHANNEL			2	EA
P014	PL 3/8" x 8" x 0'-10" w/(4) #6 x 2'-0 BENT BAR & (1) #8 x 4'-0" TAIL BAR			1	EA
P017	PL 3/8" x 3" x 0'-8" w/ (2) #5 x 2'-0"			10	EA
P020	PL 3/8" x 12" x 1'-0" w/ (4) 5/8" DIA. x 4 1/8" HCA			2	EA
P304	L 4" x 3" x 3/8" x 0'-8" w/ (2) #5 x 2'-6" & (2) #5 BENT BARS			2	EA
QLFIP127G	12T SAND PANEL ANCHOR			8	EA
MARK	DESCRIPTION			QTY.	UOM

#30109	#3 REBAR X 1'-9" LONG	18	EA
#30603	#3 REBAR X 6'-3" LONG	18	EA
#31108	#3 REBAR X 11'-8" LONG	57	EA
#50300	#5 REBAR X 3'-0" LONG	4	EA
#50709	#5 REBAR X 7'-9" LONG	2	EA
#51006	#5 REBAR X 10'-6" LONG	4	EA
#61108	#6 REBAR X 11'-8" LONG	4	EA
#6BB01	#6 BENT BAR X 4'-6" LONG	16	EA
MARK		QTY.	UOM

#70006	#7 REBAR X 0'-6" LONG	16	EA
1/2 STRAND	1/2 DIAMETER STRAND X 44'-11" LONG 30.9 KIPS	10	EA
MARK	DESCRIPTION		

CONCRETE MIX		
MIX	CY	B/F
NEP-SP	5.93	B
NEP-15	5.57	F
Fc (28 DAYS) 6,000 PSI Fc (SHIPPING) 4,000 PSI Fci (RELEASE) 3,500 PSI		

PIECES REQ'D: 1	
WEIGHT: 46600 LB	
DESIGN: IWP1.00	
PC. FOUND ON E-DRAWING: E-3.02	

REL.	DESCRIPTION	DATE	BY
1	FOR PRODUCTION	9/15/2021	BM

DRAWN:	CHECKED:	ENGR:	PLOTTED:
OSJ	BM	LMB	09/09/2021



92 REESE ROAD
MILLVILLE, NJ 08332
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com

PROJECT: HRP HUDSON BUILDING 1		
JOB NO. 20-NE0881	PIECE MARK W011	SHEET NO. 1 of 3



NOTES:

1. ALL REBAR IS TO BE 1" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO

SYMBOLS

S.I.F. = SIDE IN FORM
B.I.F. = BOTTOM IN FORM
T.I.F. = TOP IN FORM

REL.	DESCRIPTION	DATE	BY
1	FOR PRODUCTION	9/15/2021	BM

DRAWN:	CHECKED:	ENGR:	PLOTTED:
OSJ	BM	LMB	09/09/2021



NOTES:
1. ALL REBAR IS TO BE 1" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
SYMBOLS
S.I.F. = SIDE IN FORM
B.I.F. = BOTTOM IN FORM
T.I.F. = TOP IN FORM

REL.	DESCRIPTION	DATE	BY
1	FOR PRODUCTION	9/15/2021	BM

DRAWN: OSJ	CHECKED: BM	ENGR: LMB	PLOTTED: 09/09/2021
---------------	----------------	--------------	------------------------

NORTHEAST PRECAST

92 REESE ROAD
MILLVILLE, NJ 08332
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com

PROJECT: HRP HUDSON BUILDING 1		
JOB NO. 20-NE0881	PIECE MARK W011	SHEET NO. 3 of 3
