



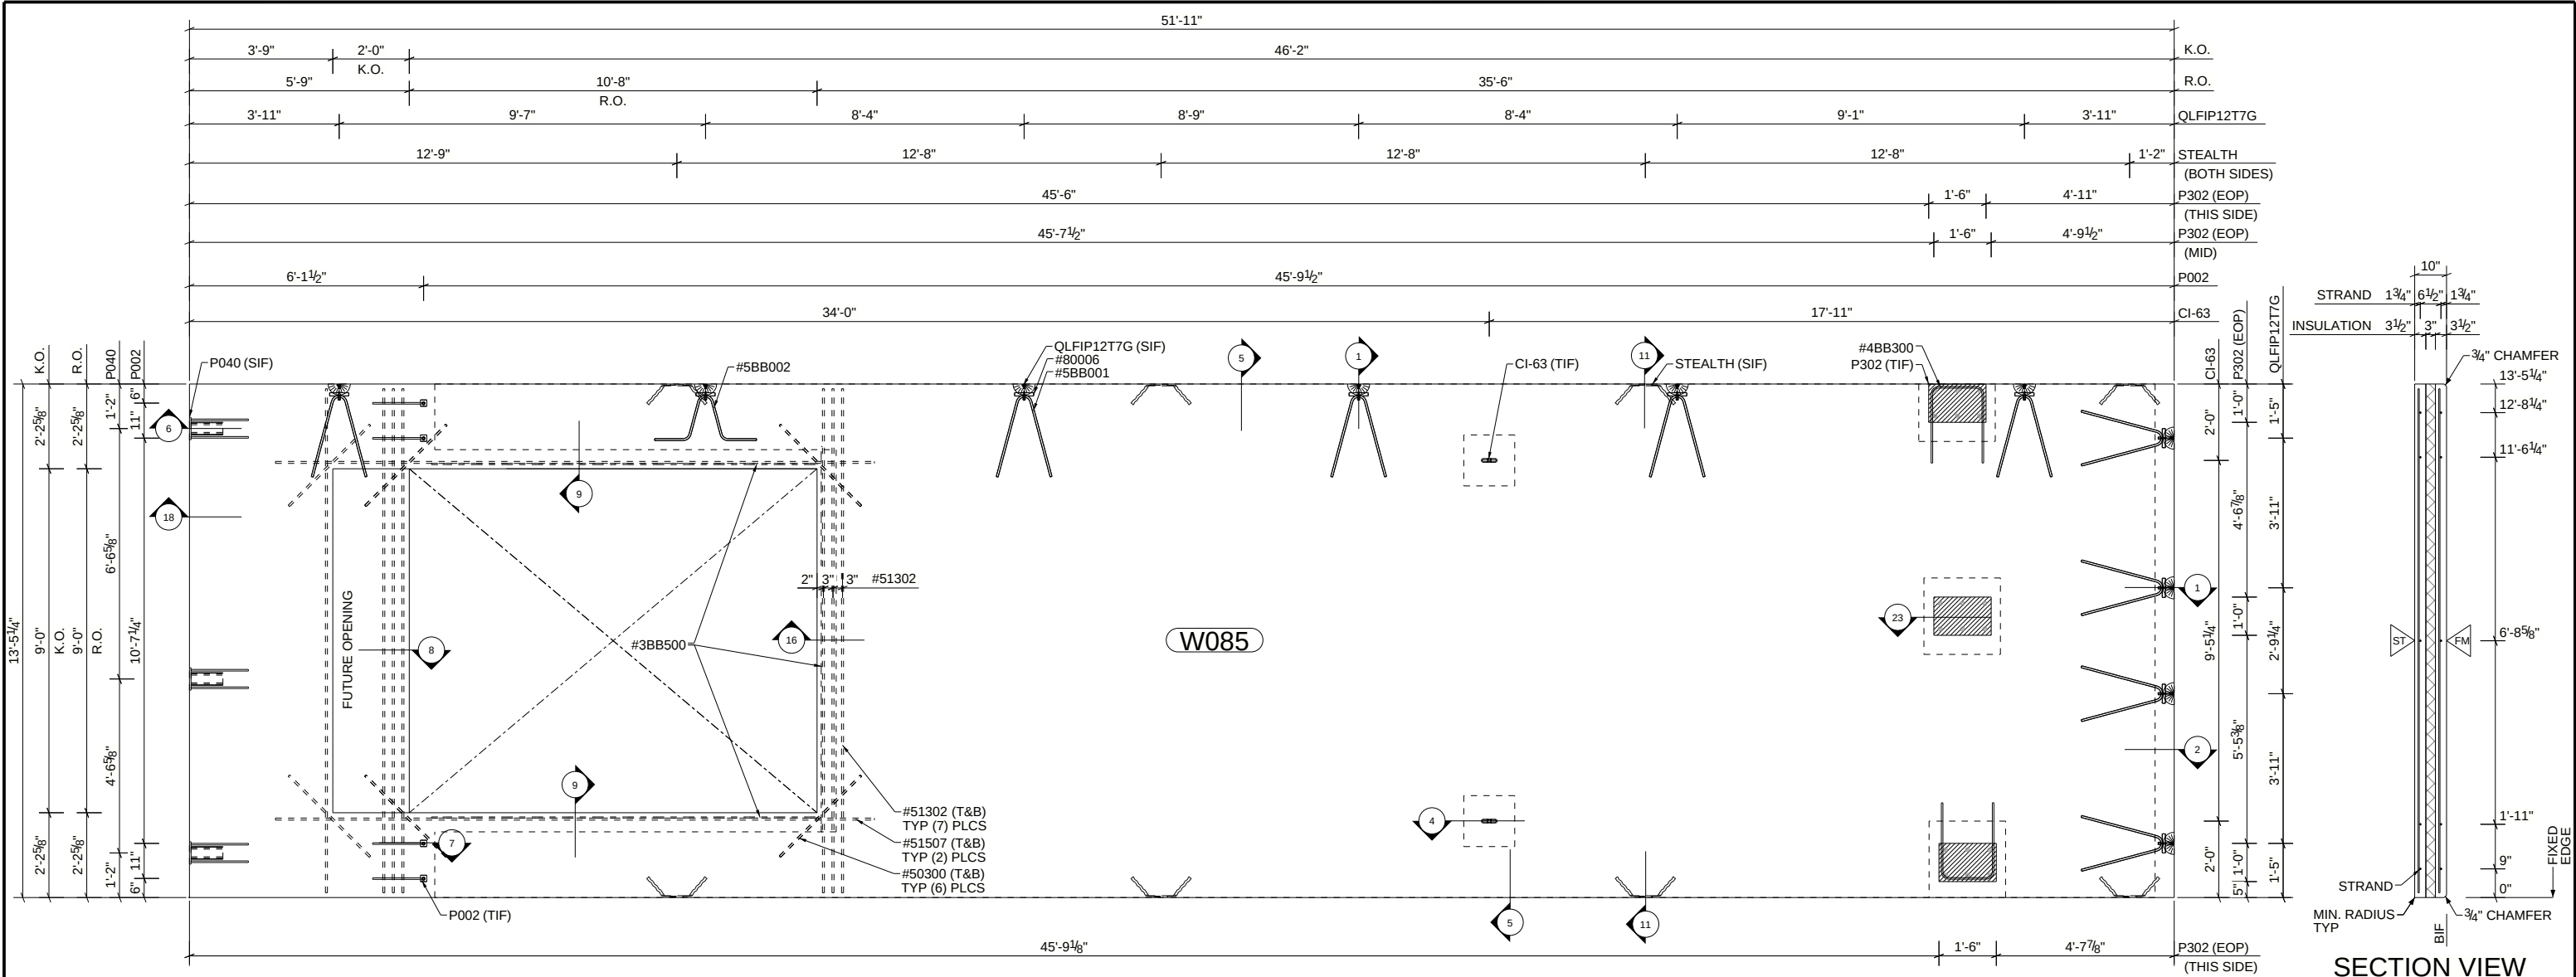

FORM VIEW

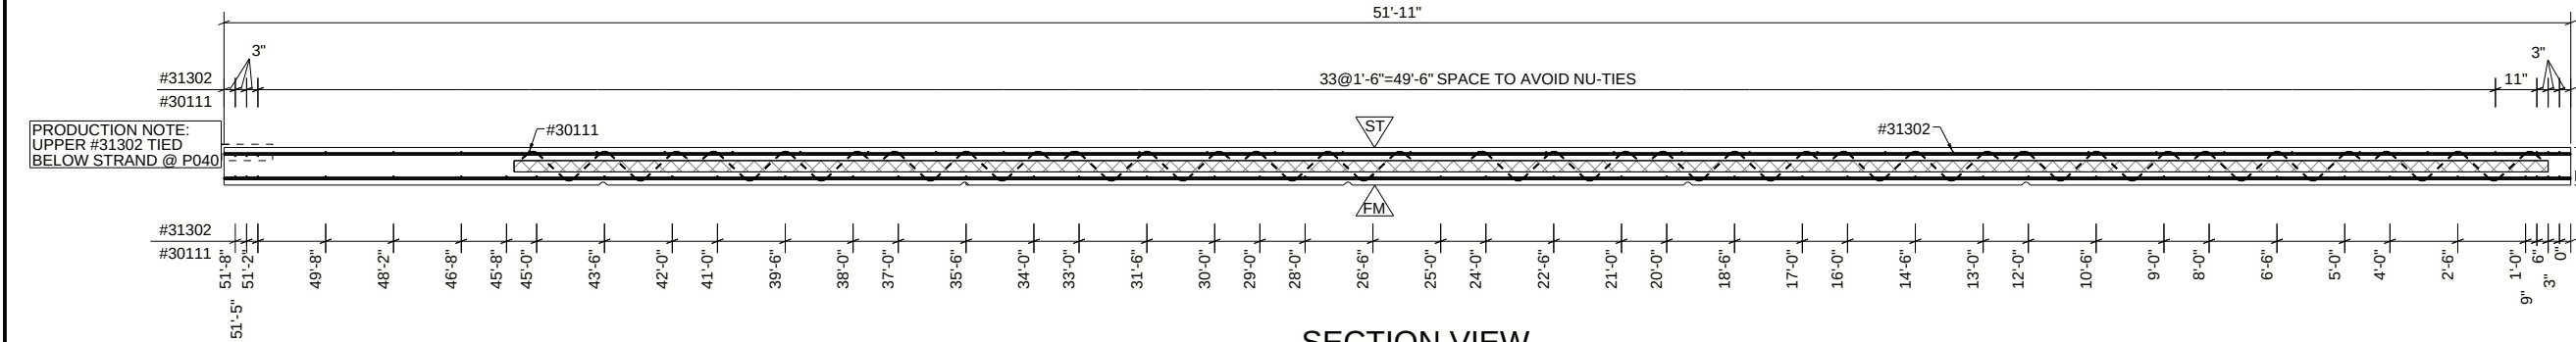

SECTION VIEW

DIAGONAL = 53'-7 9/16"

PRODUCTION NOTE:
BOTTOM WYTHE MUST BE RAKED AT ALL SOLID ZONE LOCATIONS

NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
3. ALL TRIM BARS TO BE 2" CLEAR FROM EDGE OF OPENING UNO

SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM
EOP = EDGE OF PLATE

ST = STEEL TROWEL
FM = FORM FINISH
SPX = STRAND PATTERN

CI-63	CI6334312P FLARE COIL INS 3/4 DIA X 3 1/2"	2	EA
NU-TIE	7" NU-TIE	52	EA
P002	#4 X 1'-10" FORMSAVER	4	EA
P040	PL3/4X4X0'-7" W/ (2) #4 X 1'-6"	3	EA
P302	PL1/2X1'-0"X1'-6" W/ (6) 5/8" DIA X 4 1/8 LONG HCA	3	EA
QLFI12T7G	12T SAND PANEL ANCHOR	10	EA
STEALTH	STEALTH 100 FLANGE CONNECTOR	8	EA
#30111	#3 REBAR X 1'-11" LONG	32	EA
#31302	#3 REBAR X 13'-2" LONG	67	EA
MARK	DESCRIPTION	QTY.	UOM

#3BB500	#3 BENT REBAR, SEE TABLE	3	EA
#4BB300	#4 BENT REBAR, SEE TABLE	2	EA
#50300	#5 REBAR X 3'-0" LONG	20	EA
#51302	#5 REBAR X 13'-2" LONG	14	EA
#51507	#5 REBAR X 15'-7" LONG	4	EA
#5BB001	#5 BENT REBAR, SEE TABLE	18	EA
#5BB002	#5 BENT REBAR, SEE TABLE	2	EA
#80006	#8 REBAR X 0'-6" LONG	20	EA
1/2 STRAND	1/2 DIAMETER STRAND 28.90 Kips	10	EA
MARK	DESCRIPTION	QTY.	UOM

MARK	DESCRIPTION	QTY.	UOM
------	-------------	------	-----

CONCRETE MIX		
MIX	CY	B/F
725N	7.55	B
700A	6.50	F
F _c (28 DAYS)		
6000 PSI		
F _c (SHIPPING)		
5000 PSI		
F _c (RELEASE)		
3500 PSI		


PIECES REQD:	1
WEIGHT:	57084 LBS
DESIGN:	SP1
CONTROL NO.:	085

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	07/01/2025	JOM
1			
2			
3			
4			
5			
DRAWN:	CHECKED:	ENGR:	PLOTTED:
JOM	AMC	AJC	07/14/2025

NORTHEAST PRECAST

4081 S. LINCOLN AVE
VINELAND, NJ 08361
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com

PROJECT: NEWBURGH SOUTH LOGISTICS CENTER
JOB NO. 25-NE1212
PIECE MARK: W085
SHEET NO. 1 OF 3

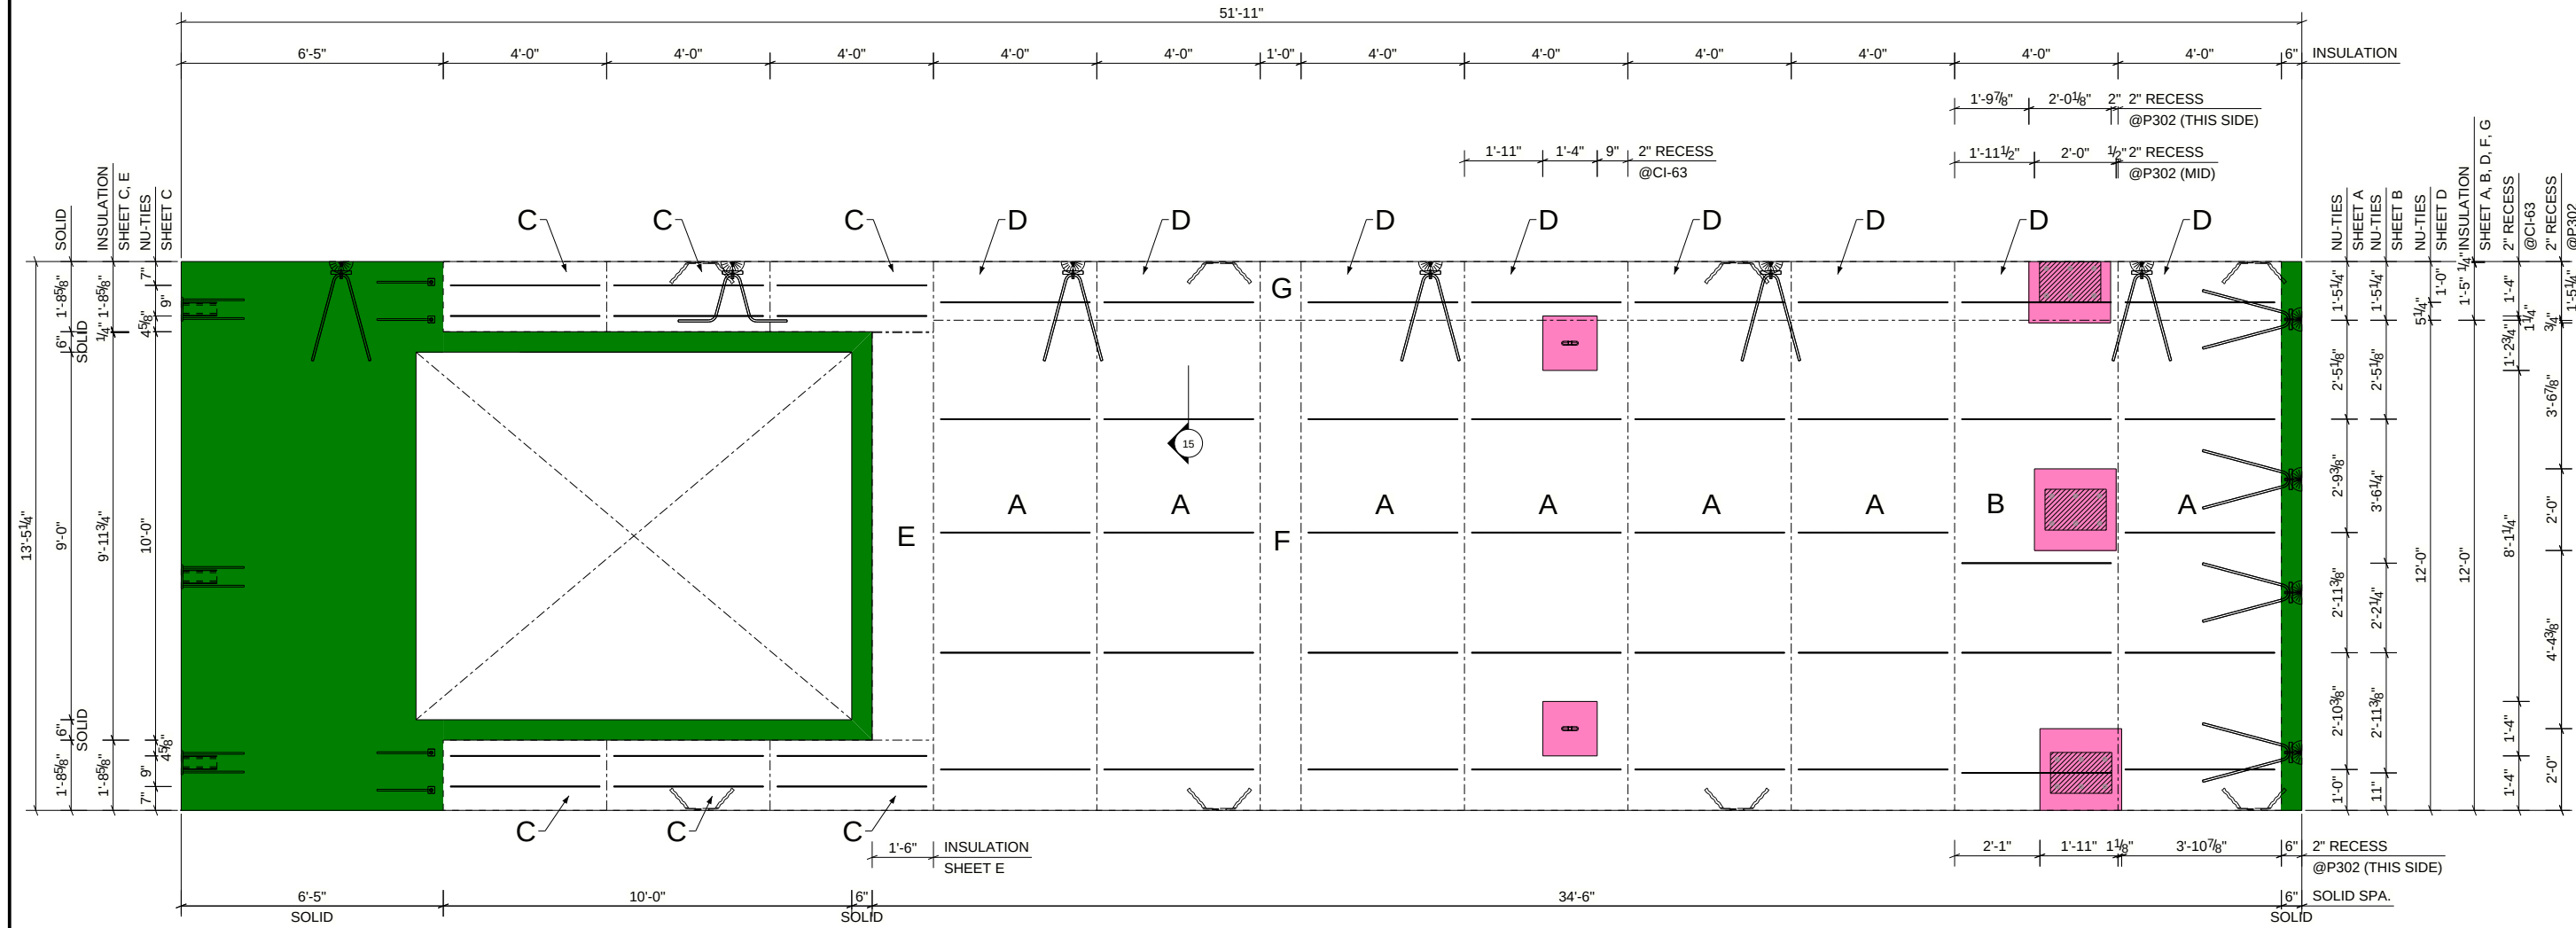

FOAM DRAWING

PIECES OF 3" 1.25# EPS:
A/B: (8) PIECES @ 4'-0" X 12'-0"
C: (6) PIECES @ 4'-0" X 1'-8 5/8"
D: (8) PIECES @ 4'-0" X 1'-5"
E: (1) PIECE @ 1'-6" X 9'-11 3/4"
F: (1) PIECE @ 1'-0" X 12'-0"
G: (1) PIECE @ 1'-0" X 1'-5"

PIECES OF 1" 1.25# EPS:
CI-63: (2) 1'-4" X 1'-4"
P302: (3) 2'-0" X 2'-0"

NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM



REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	07/01/2025	JOM
1			
2			
3			
4			
5			

DRAWN:	CHECKED:	ENGR:	PLOTTED:
JOM	AMC	AJC	07/14/2025

NORTHEAST PRECAST
4081 S. LINCOLN AVE
VINELAND, NJ 08361
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com


PROJECT: NEWBURGH SOUTH LOGISTICS CENTER

JOB NO.	PIECE MARK	SHEET NO.
25-NE1212	W085	2 OF 3

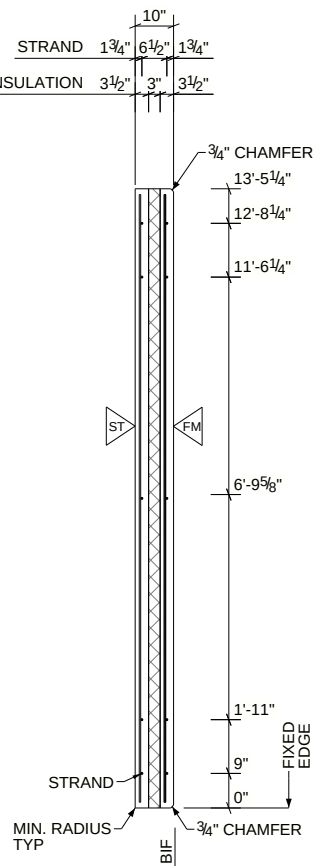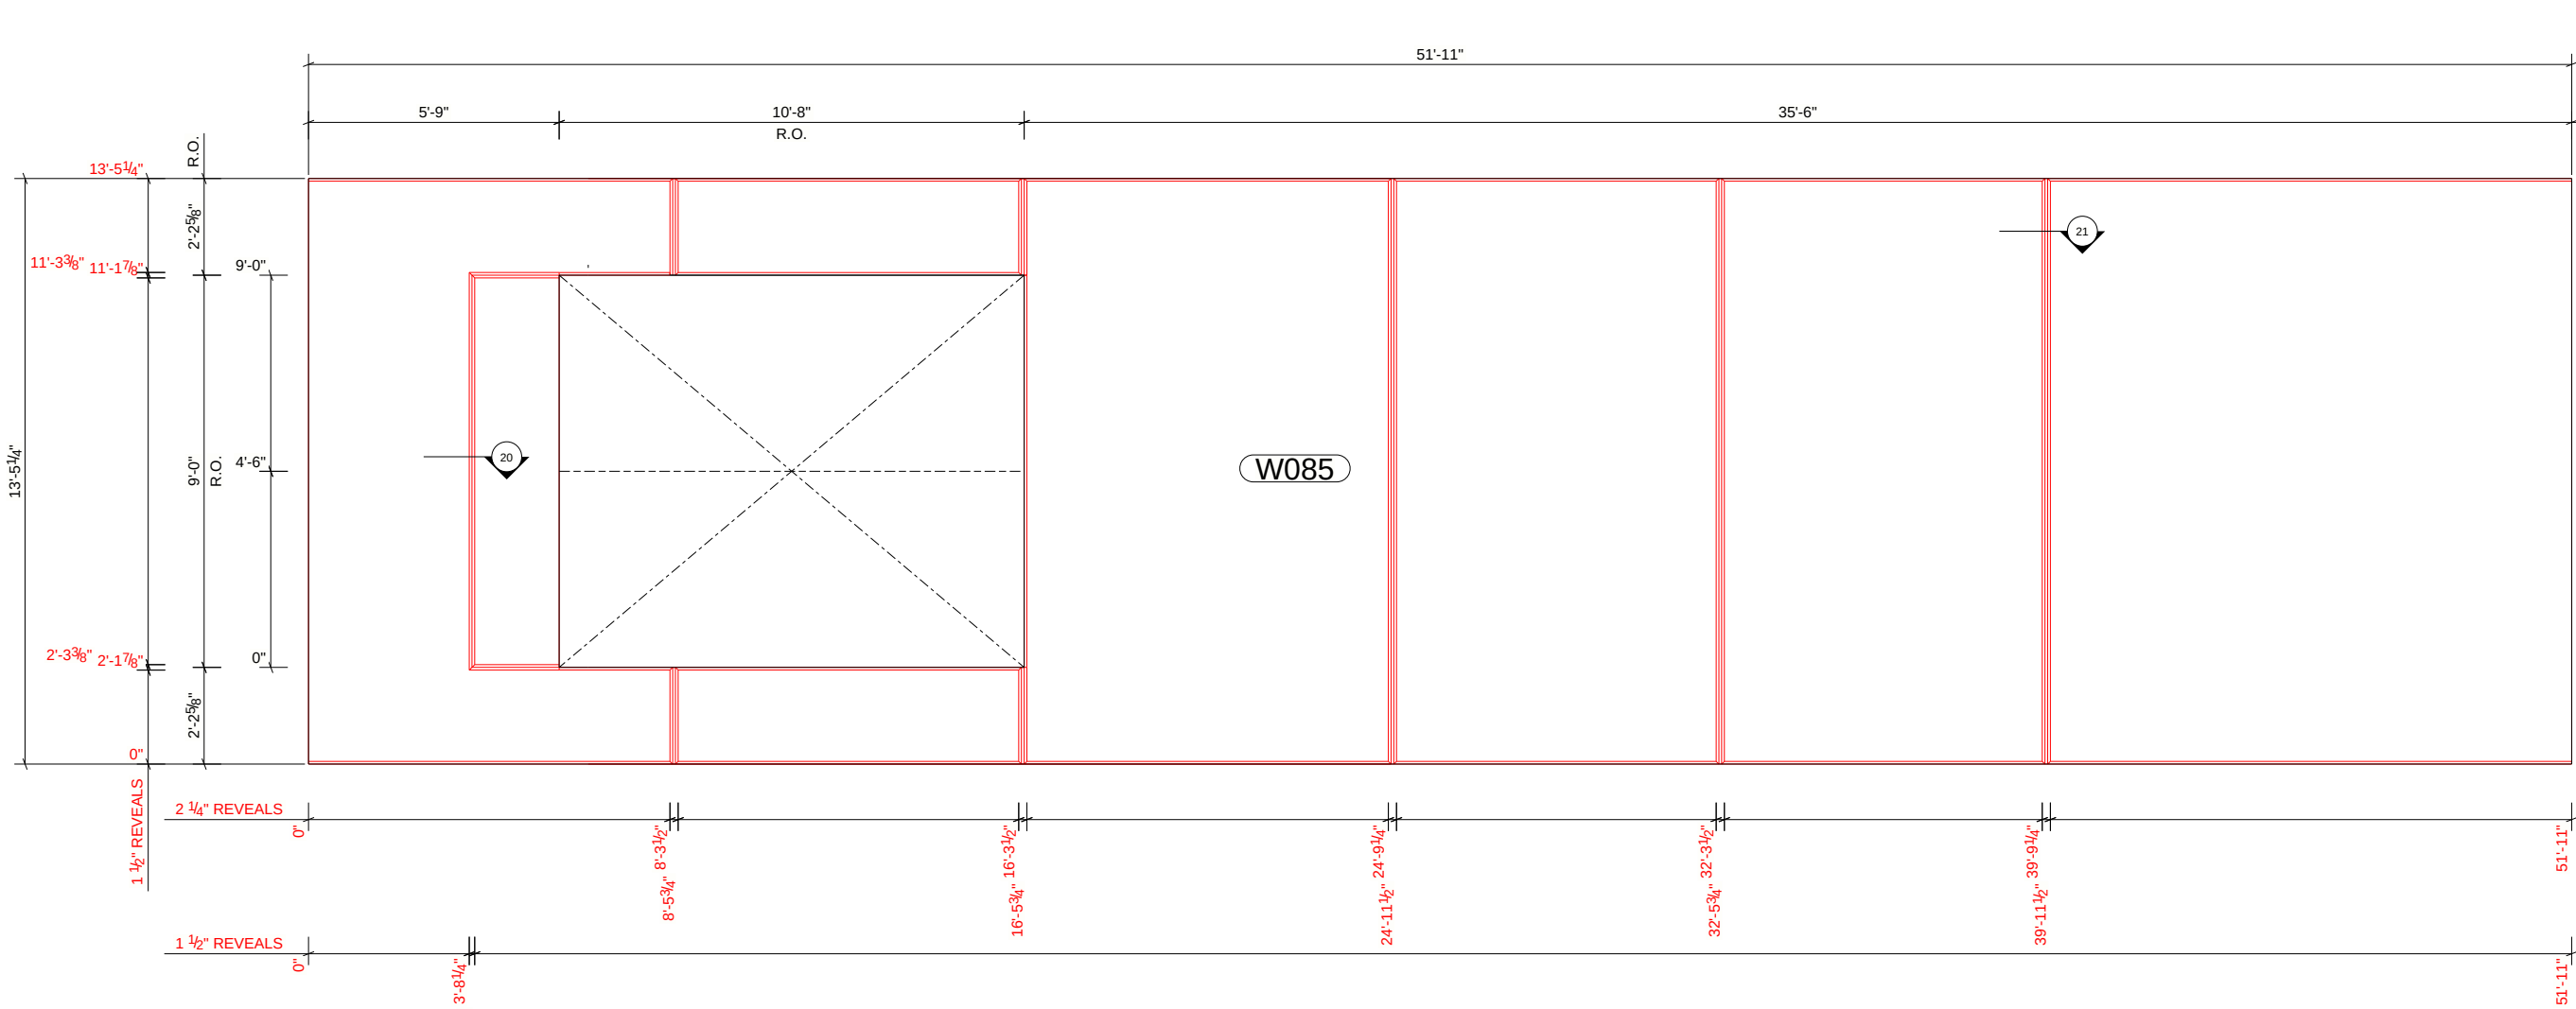

SECTION VIEW

REVEAL DRAWING

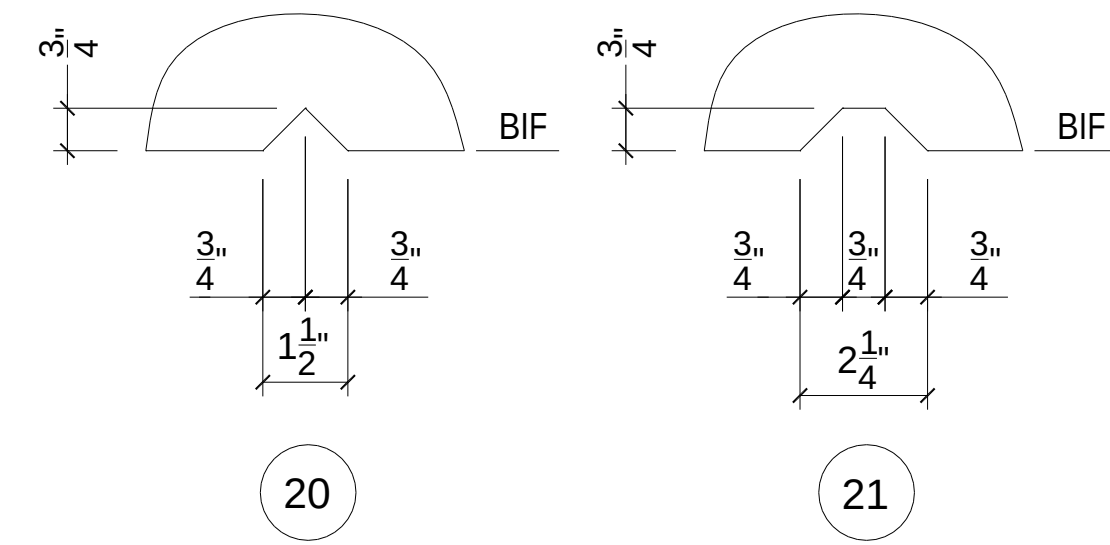

NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	07/01/2025	JOM
1			
2			
3			
4			
5			

DRAWN: JOM	CHECKED: AMC	ENGR: AJC	PLOTTED: 07/14/2025
---------------	-----------------	--------------	------------------------

NORTHEAST PRECAST
4081 S. LINCOLN AVE
VINELAND, NJ 08361
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com

PROJECT:
NEWBURGH SOUTH LOGISTICS CENTER

JOB NO.
25-NE1212

PIECE MARK
W085

SHEET NO.
3 OF 3
