



ROTATE PANEL

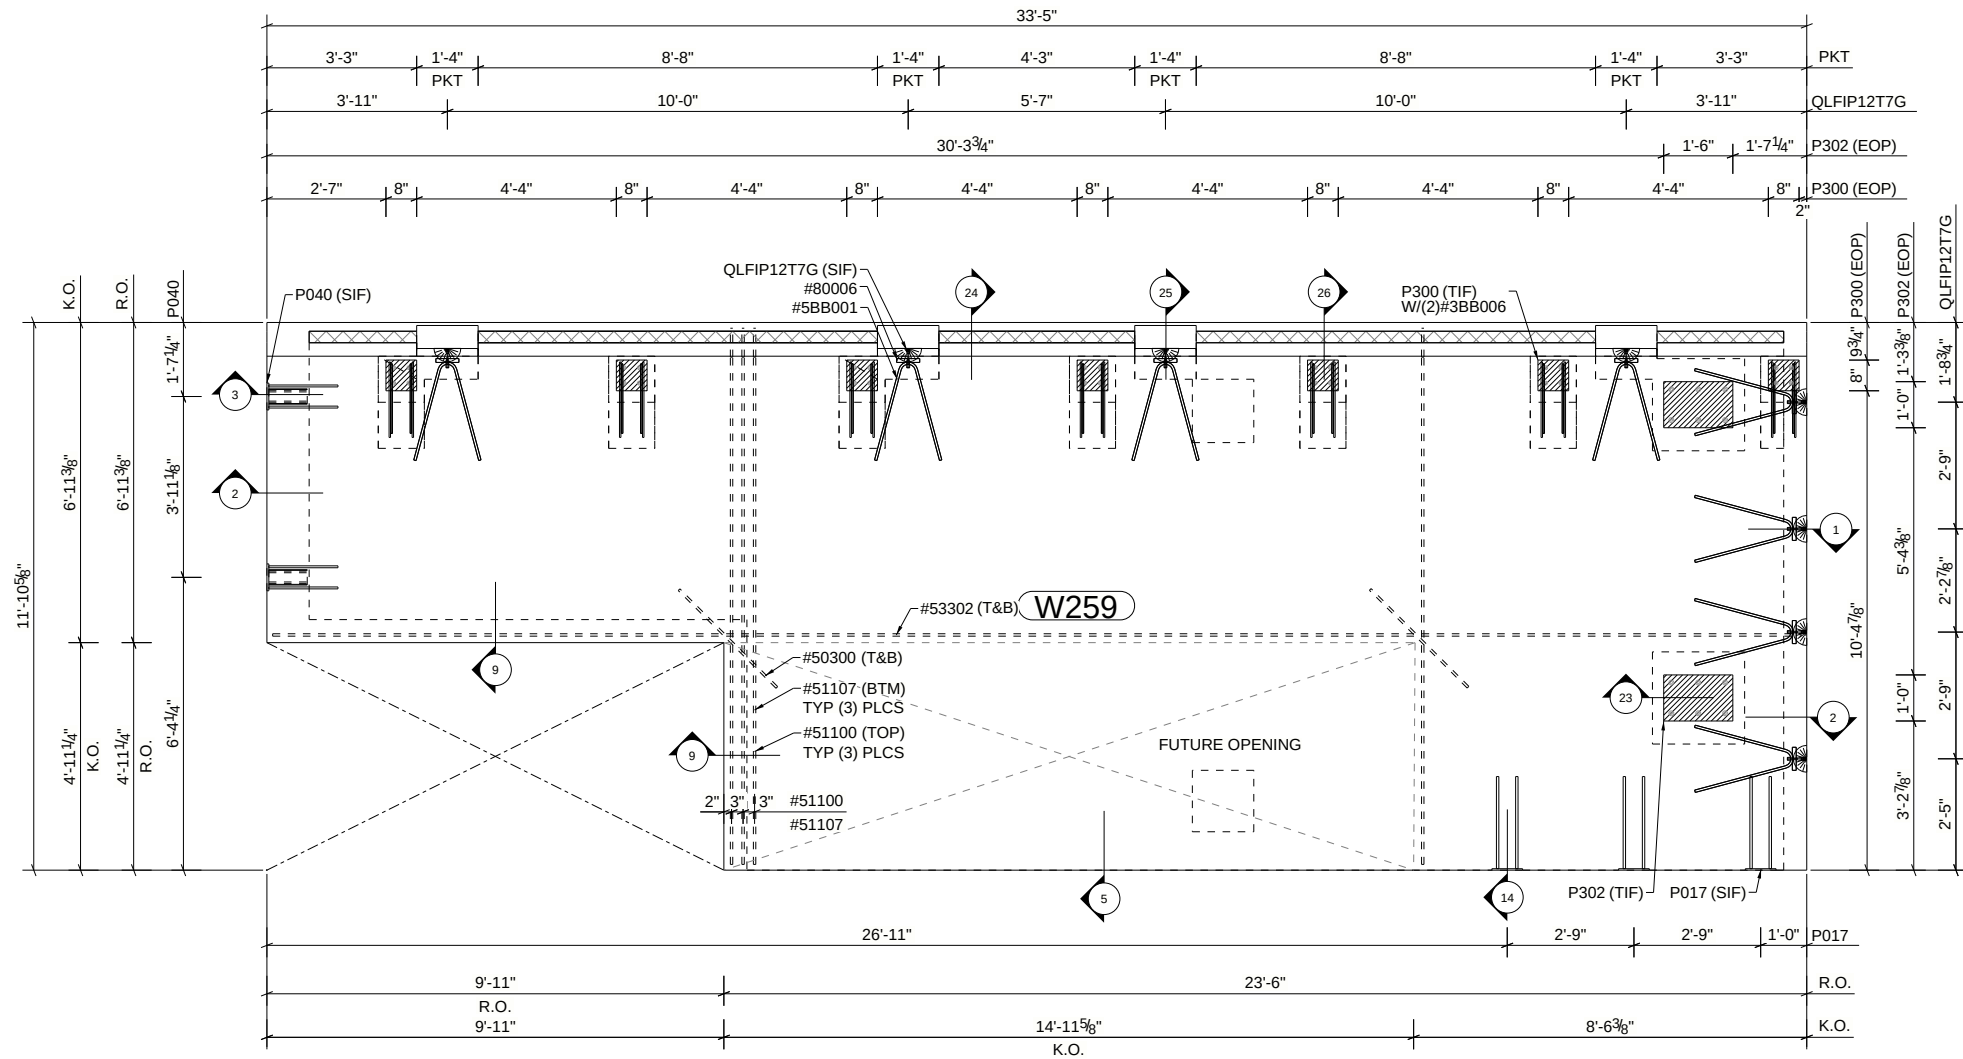


FORM VIEW

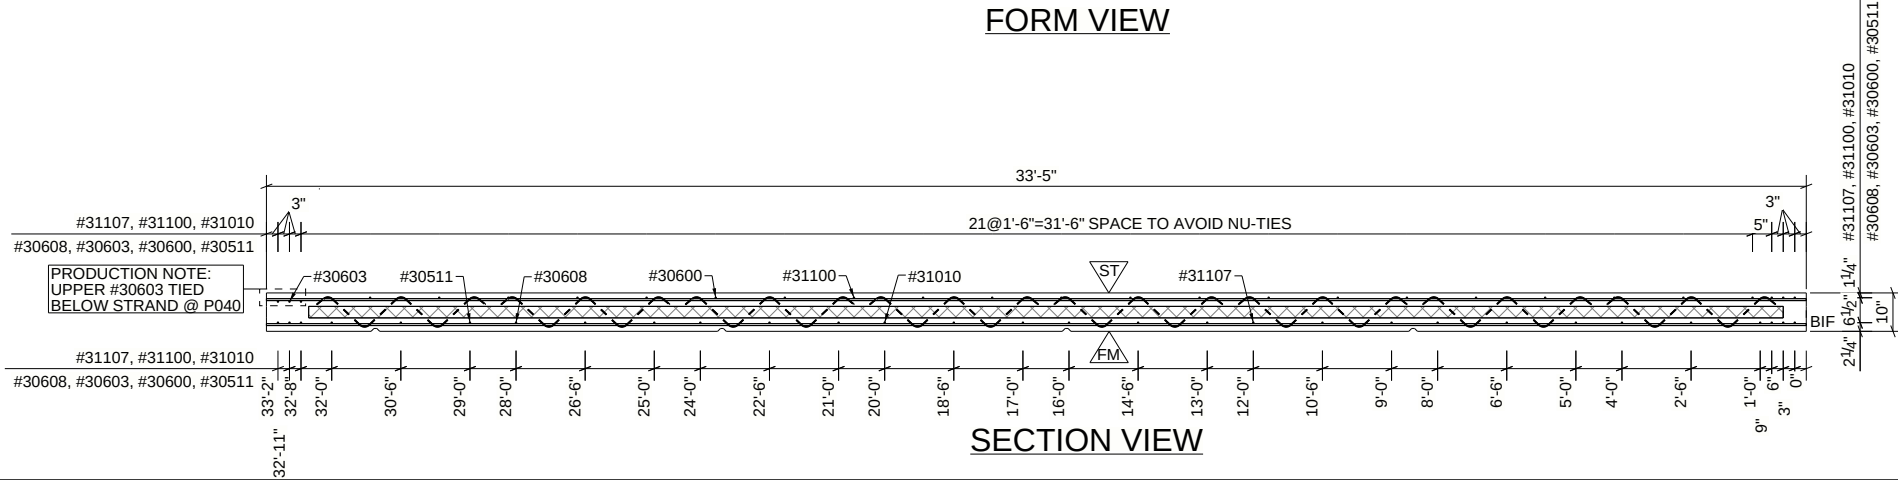

SECTION VIEW

Deflect 1'-0" Strand UP 1" to 1'-1"

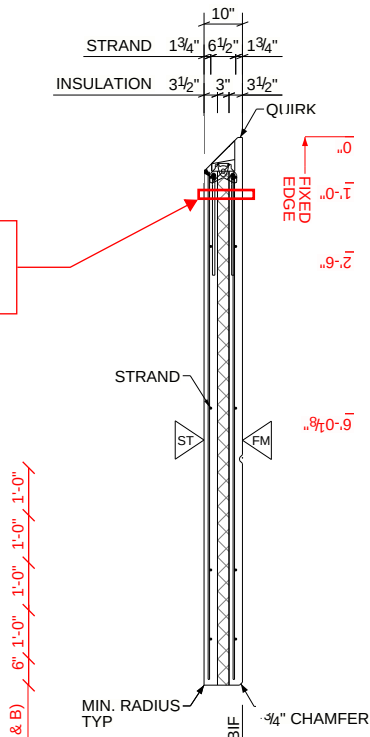

SECTION VIEW

DIAGONAL = 35'-5 5/8"

PRODUCTION NOTE:
BOTTOM WYTHE MUST BE RAKED AT ALL SOLID ZONE LOCATIONS

- NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
 2. ALL DIMENSIONS ARE TO CENTERLINE UNO
 3. ALL TRIM BARS TO BE 2" CLEAR FROM EDGE OF OPENING UNO

SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM
EOP = EDGE OF PLATE

ST = STEEL TROWEL
FM = FORM FINISH
SPX = STRAND PATTERN

NU-TIE	7" NU-TIE	34	EA
P017	PL3/8X3X0'-8" W/ (2) #5 X 2'-0"	3	EA
P040	PL3/4X4X0'-7" W/ (2) #4 X 1'-6"	2	EA
P300	PL3/8X8X8 W/ (4) 1/2" DIA X 6" LONG HCA & (2) #4 BARS	7	EA
P302	PL1/2X1'-0"X1'-6" W/ (6) 5/8" DIA X 4 1/8 LONG HCA	2	EA
QLFIP12T7G	12T SAND PANEL ANCHOR	8	EA
#30511	#3 REBAR X 5'-11" LONG	1	EA
#30600	#3 REBAR X 6'-0" LONG	6	EA
#30603	#3 REBAR X 6'-3" LONG	3	EA
MARK	DESCRIPTION	QTY.	UOM

#30608	#3 REBAR X 6'-8" LONG	9	EA
#31010	#3 REBAR X 10'-10" LONG	3	EA
#31100	#3 REBAR X 11'-0" LONG	18	EA
#31107	#3 REBAR X 11'-7" LONG	17	EA
#3BB006	#3 BENT REBAR, SEE TABLE	14	EA
#50300	#5 REBAR X 3'-0" LONG	4	EA
#51100	#5 REBAR X 11'-0" LONG	4	EA
#51107	#5 REBAR X 11'-7" LONG	4	EA
#53302	#5 REBAR X 33'-2" LONG	2	EA
MARK	DESCRIPTION	QTY.	UOM

#5BB001	#5 BENT REBAR, SEE TABLE	16	EA
#80006	#8 REBAR X 0'-6" LONG	16	EA
1/2 STRAND	1/2 DIAMETER STRAND 28.90 Kips	10	EA
#52300		10	EA
MARK	DESCRIPTION	QTY.	UOM

CONCRETE MIX		
MIX	CY	B/F
725N	4.11	B
700A	3.54	F
F _c (28 DAYS)		
6000	PSI	
F _c (SHIPPING)		
4000	PSI	
F _c (RELEASE)		
3500	PSI	

PIECES REQ'D:
1
WEIGHT:
31173 LBS
DESIGN:
SP4
CONTROL NO.:
259

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	07/01/2025	JOM
1			
2			
3			
4			
5			
BROWN	CHECKED	ENGR	PLOTTED
JOM	AMC	AJC	08/21/2025

NORTHEAST PRECAST


4081 S. LINCOLN AVE
VINELAND, NJ 08361
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com

PROJECT:
NEWBURGH SOUTH LOGISTICS CENTER

JOB NO.:
25-NE1212

PIECE MARK:
W259

SHEET NO.:
1 OF 3

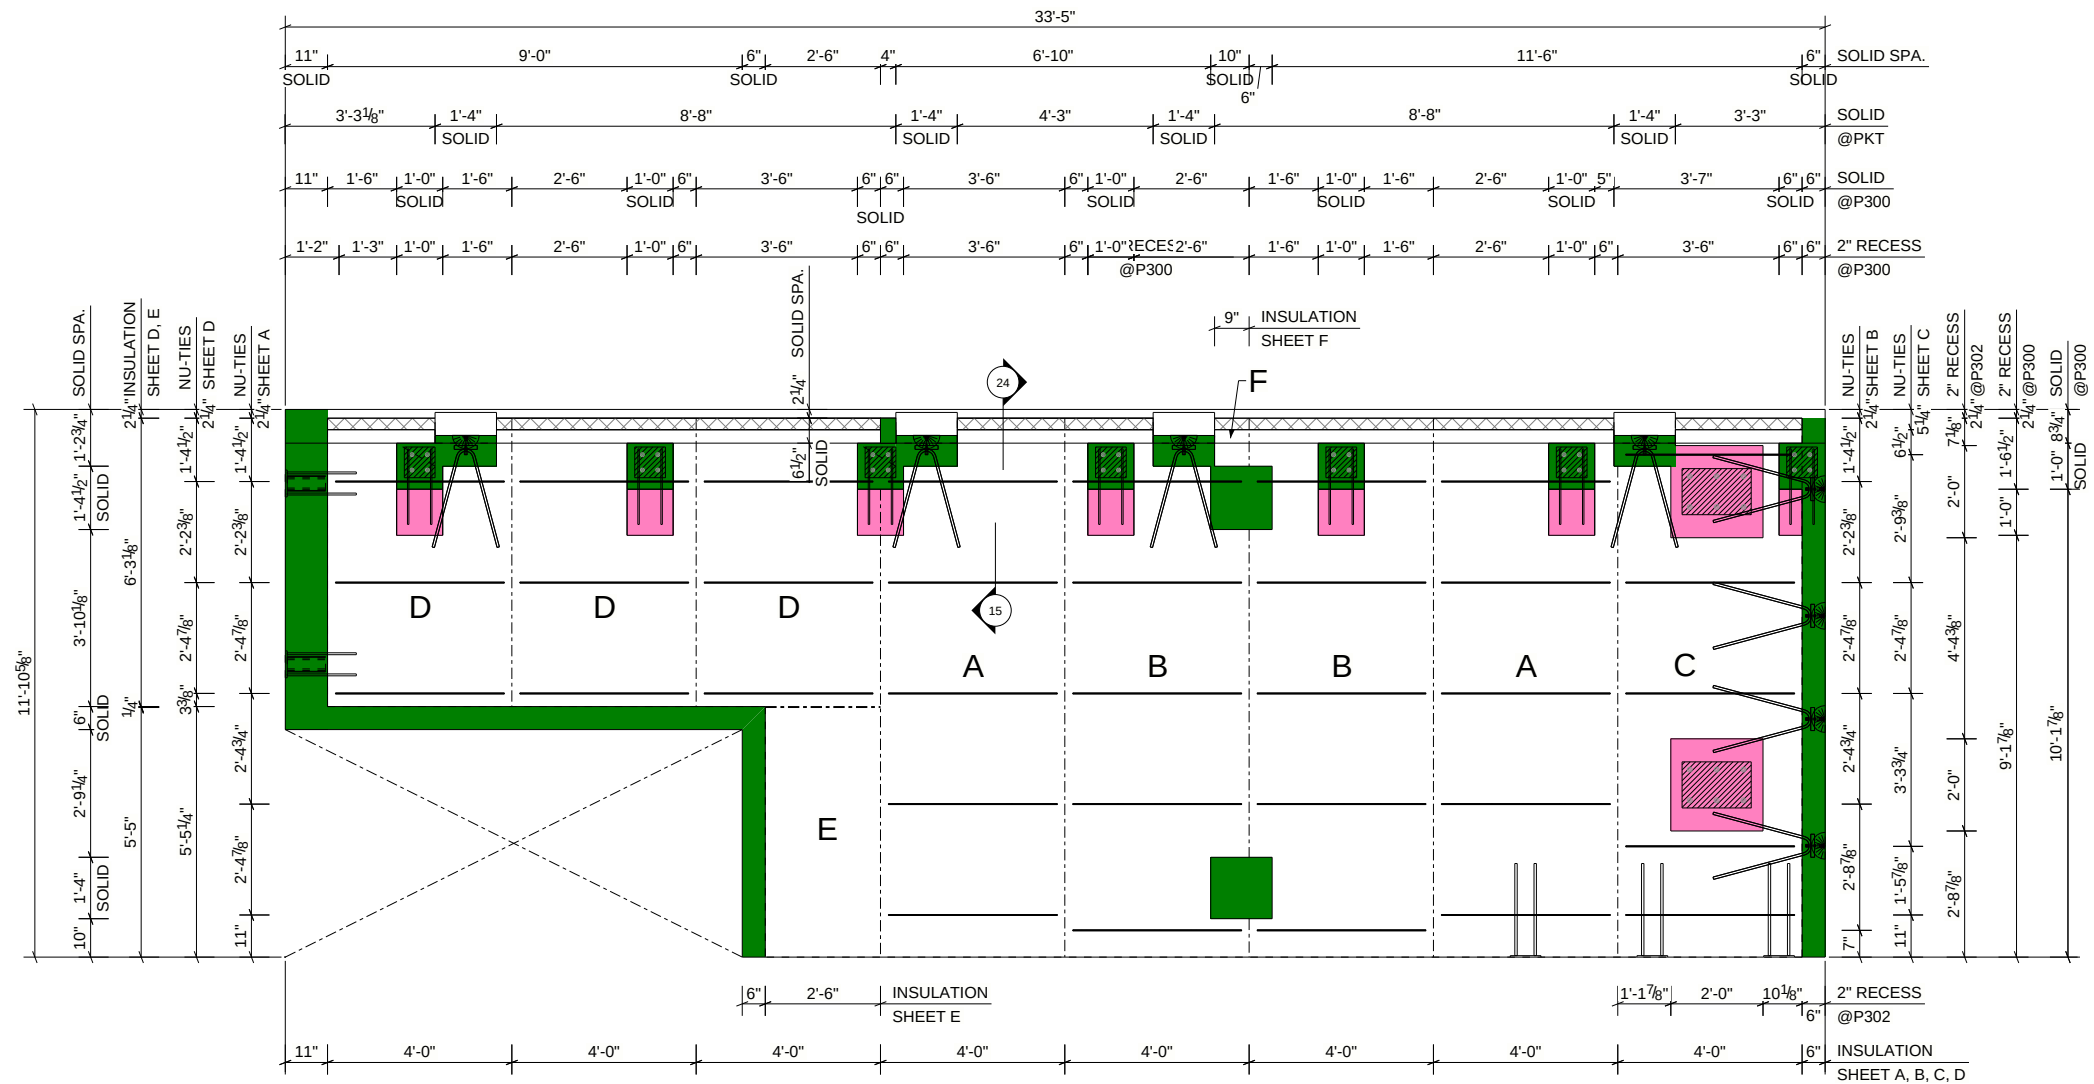


FOAM DRAWING

PIECES OF 3" 1.25# EPS:
 A/B/C: (5) PIECES @ 4'-0" X 10'-7 7/8"
 D: (3) PIECES @ 4'-0" X 6'-3 1/8"
 E: (1) PIECE @ 2'-6" X 5'-5"
 F: (1) PIECE @ 0'-9" X 1'-0 1/2"

PIECES OF 1" 1.25# EPS:
 P300: (7) 1'-0" X 1'-0"
 P302: (2) 2'-0" X 2'-0"

NOTES:
 1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
 2. ALL DIMENSIONS ARE TO CENTERLINE UNO
 SYMBOLS
 SIF = SIDE IN FORM
 BIF = BOTTOM IN FORM
 TIF = TOP IN FORM

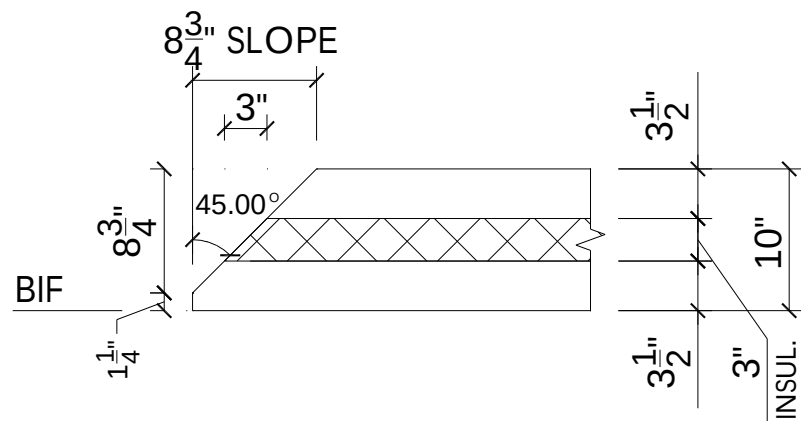

24




REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	07/01/2025	JOM
1			
2			
3			
4			
5			

DRAWN: JOM	CHECKED: AMC	ENGR: AJC	PLOTTED: 08/21/2025
---------------	-----------------	--------------	------------------------

**NORTHEAST
PRECAST**
 4081 S. LINCOLN AVE
 VINELAND, NJ 08361
 OFFICE: 866-699-2557 FAX: 856-765-9087
 www.northeastprecast.com

PROJECT:
NEWBURGH SOUTH LOGISTICS CE***
 JOB NO. 25-NE1212
 SHEET NO. 2 OF 3

ROTATE PANEL

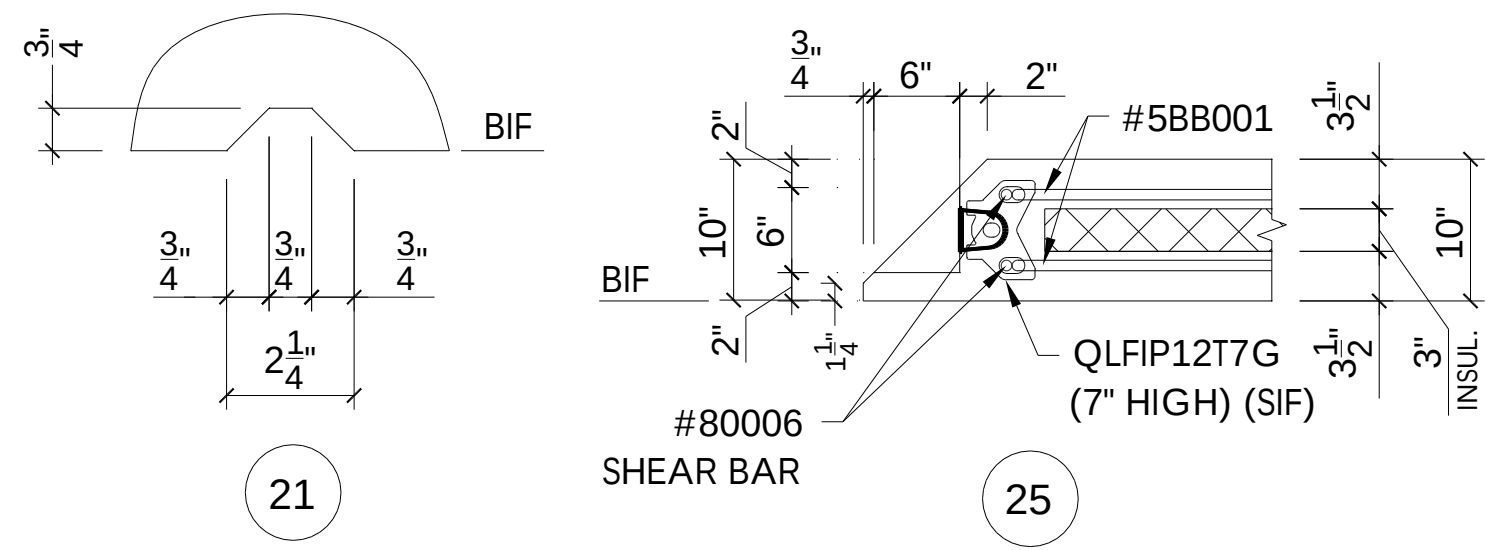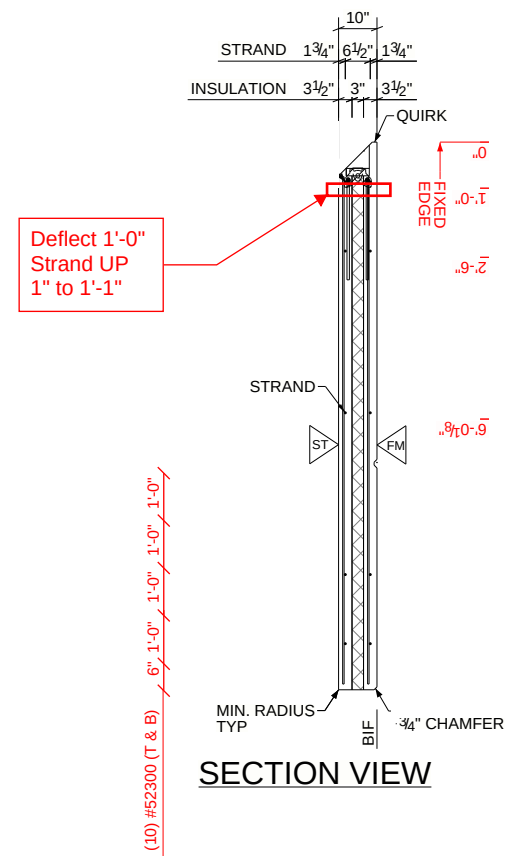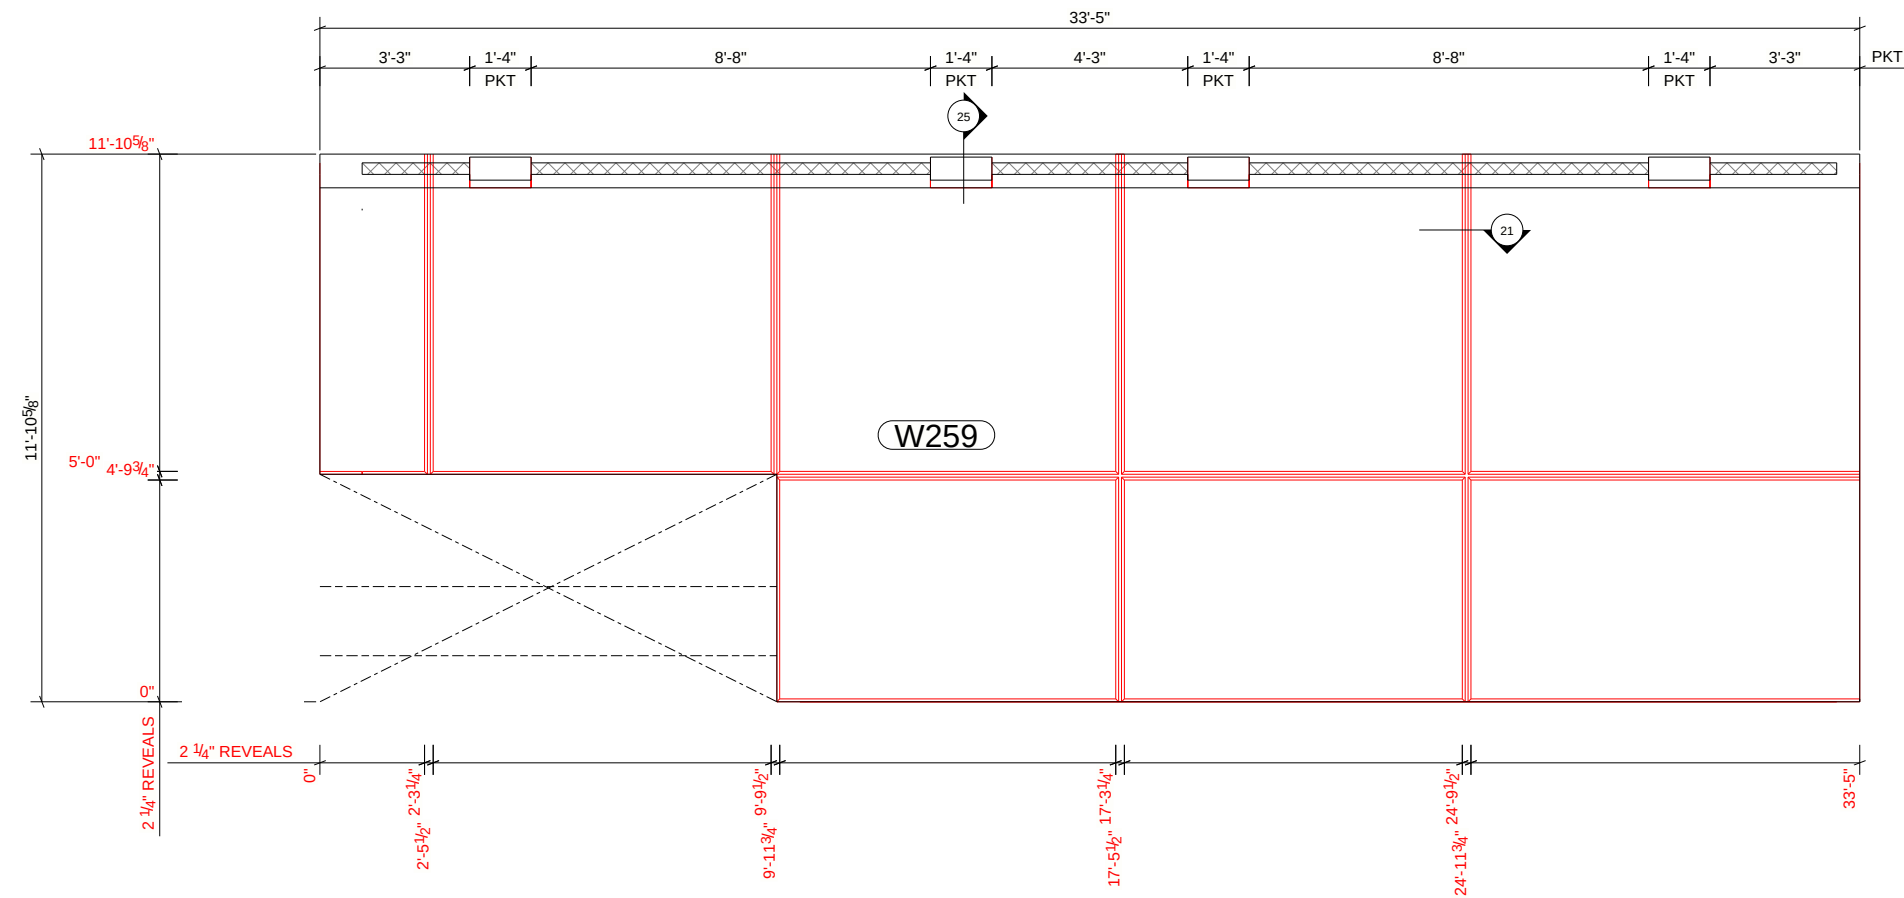

NOTES:

1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO

SYMBOLS

SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	07/01/2025	JOM
1			
2			
3			
4			
5			

DRAWN: JOM	CHECKED: AMC	ENGR: AJC	PLOTTED: 08/21/2025
---------------	-----------------	--------------	------------------------

PROJECT: NEWBURGH SOUTH LOGISTICS CE***		SHEET NO. 3 OF 3
JOB NO. 25-NE1212	PIECE MARK W259	

NORTHEAST PRECAST	
4081 S. LINCOLN AVE VINELAND, NJ 08361 OFFICE: 866-699-2557 FAX: 856-765-9087 www.northeastprecast.com	
