




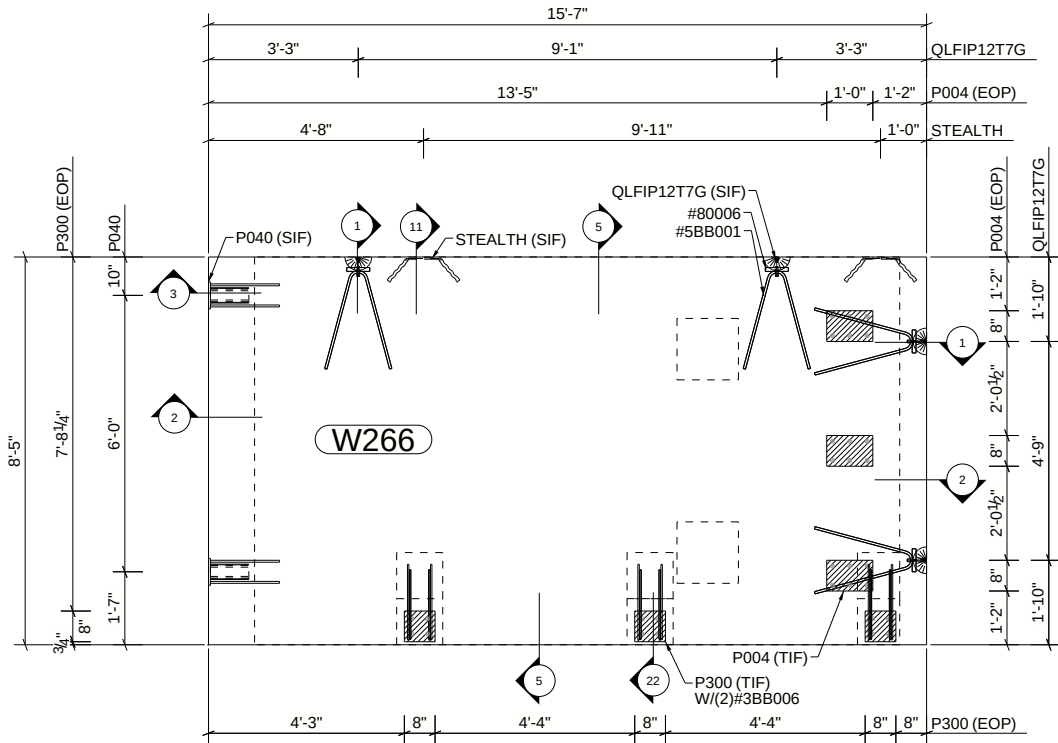

FORM VIEW

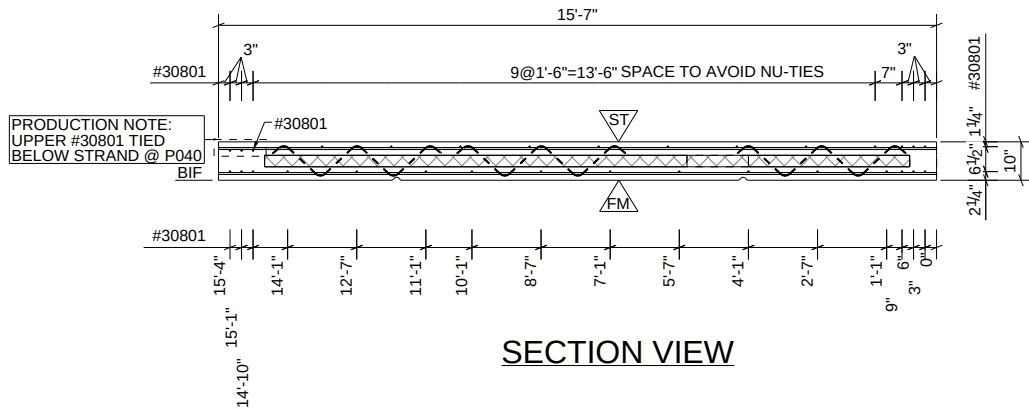

SECTION VIEW

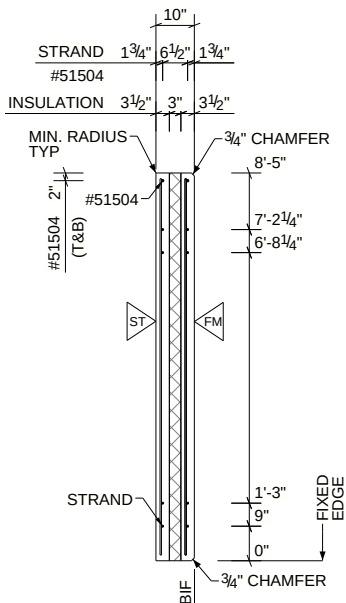

SECTION VIEW

DIAGONAL = 17'-8 9/16"

PRODUCTION NOTE:
BOTTOM WYTHE MUST BE RAKED AT
ALL SOLID ZONE LOCATIONS

NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
3. ALL TRIM BARS TO BE 2" CLEAR FROM EDGE
OF OPENING UNO

SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM
EOP = EDGE OF PLATE

ST = STEEL TROWEL
FM = FORM FINISH
SPX = STRAND PATTERN

NU-TIE	7" NU-TIE	12	EA
P004	PL3/8X8X1'-0" W/ (6) 1/2" DIA X 2 5/8" HCA	3	EA
P040	PL3/4X4X0'-7" W/ (2) #4 X 1'-6"	2	EA
P300	PL3/8X8X8 W/ (4) 1/2" DIA X 6" LONG HCA & (2) #4 BARS	3	EA
QLFI12T7G	12T SAND PANEL ANCHOR	4	EA
STEALTH	STEALTH 100 FLANGE CONNECTOR	2	EA
#30801	#3 REBAR X 8'-1" LONG	31	EA
#3BB006	#3 BENT REBAR, SEE TABLE	6	EA
#51504	#5 REBAR X 15'-4" LONG	2	EA
MARK	DESCRIPTION	QTY.	UOM

#5BB001	#5 BENT REBAR, SEE TABLE	8	EA
#80006	#8 REBAR X 0'-6" LONG	8	EA
1/2 STRAND	1/2 DIAMETER STRAND 28.90 Kips	8	EA
MARK	DESCRIPTION	QTY.	UOM


MARK	DESCRIPTION	QTY.	UOM

CONCRETE MIX		
MIX	CY	B/F
725N	1.61	B
700A	1.42	F
F _c (28 DAYS)		
6000 PSI		
F _c (SHIPPING)		
4000 PSI		
F _c (RELEASE)		
3500 PSI		

PIECES REQ'D:	1
WEIGHT:	12361 LBS
DESIGN:	SP3
CONTROL NO.:	266

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	08/07/2025	IJH
1			
2			
3			
4			
5			
DRAWN:	CHECKED:	ENGR:	PLOTTED:
IJH	AMC	AJC	08/20/2025

NORTHEAST PRECAST		
4081 S. LINCOLN AVE VINELAND, NJ 08361 OFFICE: 866-699-2557 FAX: 856-765-9087 www.northeastprecast.com		
PROJECT:	NEWBURGH SOUTH LOGISTICS CENTER	
JOB NO.	PIECE MARK	SHEET NO.
25-NE1212	W266	1 OF 3

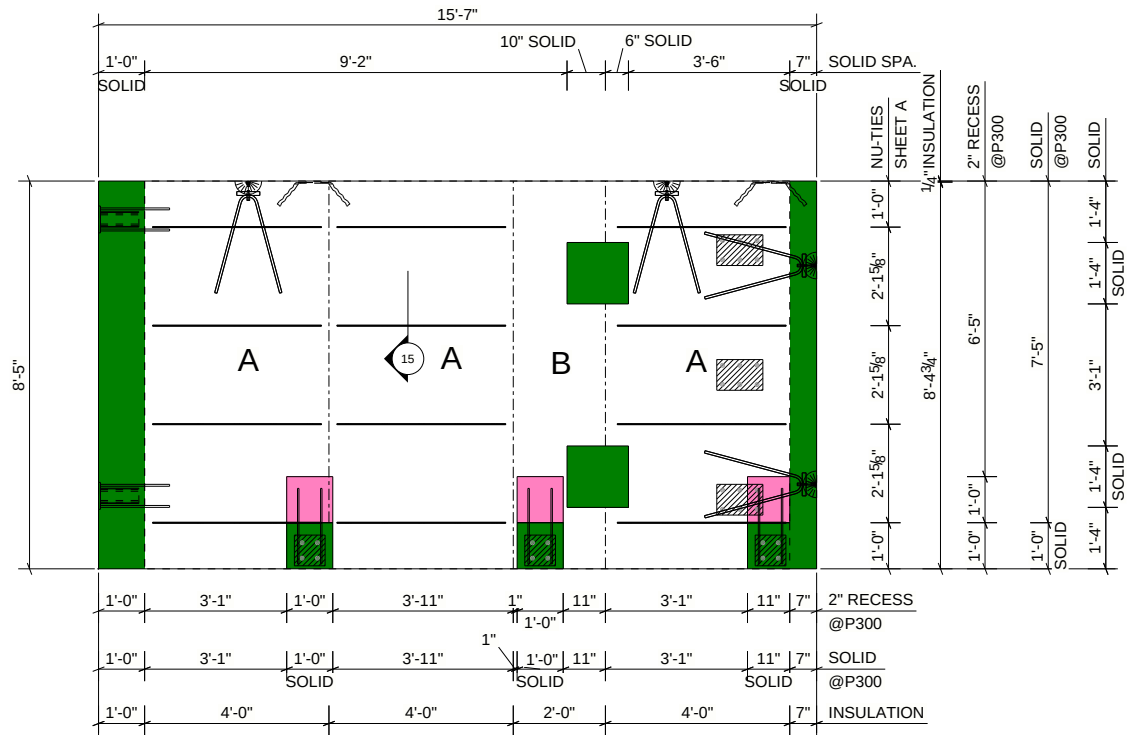

FOAM DRAWING

PIECES OF 3" 1.25# EPS:
A: (3) PIECES @ 4'-0" X 8'-4 3/4"
B: (1) PIECE @ 2'-0" X 8'-4 3/4"

PIECES OF 1" 1.25# EPS:
P300: (3) 1'-0" X 1'-0"


NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	08/07/2025	IJH
1			
2			
3			
4			
5			


DRAWN: IJH	CHECKED: AMC	ENGR: AJC	PLOTTED: 08/20/2025
---------------	-----------------	--------------	------------------------

**NORTHEAST
PRECAST**
4081 S. LINCOLN AVE
VINELAND, NJ 08361
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com


PROJECT: NEWBURGH SOUTH LOGISTICS CENTER	PIECE MARK: W266	SHEET NO.: 2 OF 3
---	---------------------	----------------------

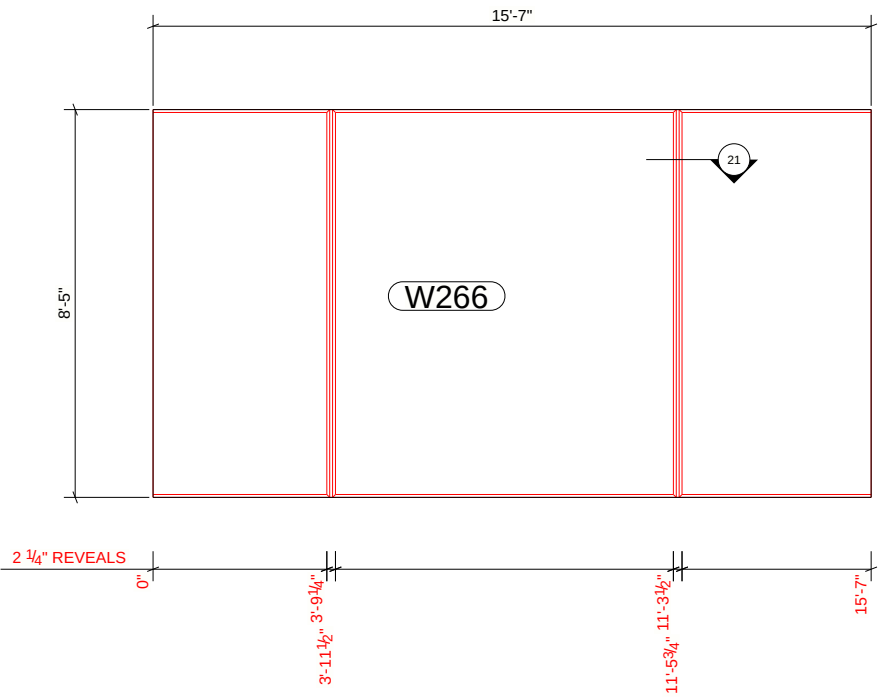

REVEAL DRAWING

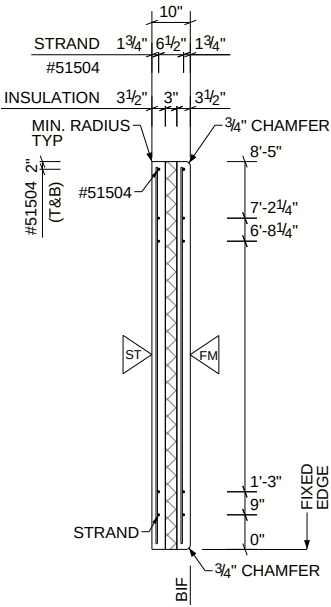

SECTION VIEW

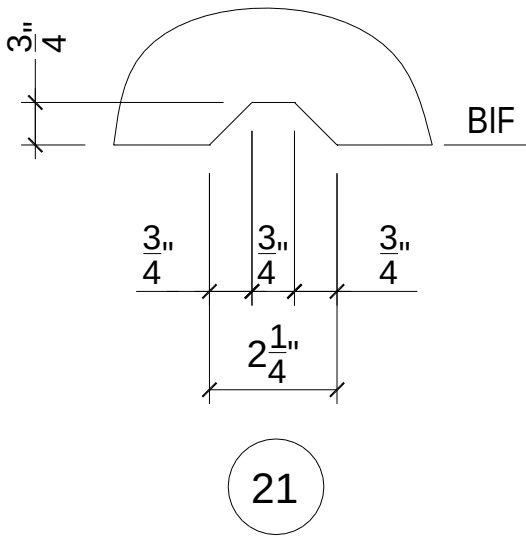

NOTES:
1. ALL REBAR IS TO BE 1 1/2" CLR. UNO
2. ALL DIMENSIONS ARE TO CENTERLINE UNO
SYMBOLS
SIF = SIDE IN FORM
BIF = BOTTOM IN FORM
TIF = TOP IN FORM

REV.	DESCRIPTION	DATE	BY
0	ISSUED FOR PRODUCTION	08/07/2025	IJH
1			
2			
3			
4			
5			

DRAWN: IJH	CHECKED: AMC	ENGR: AJC	PLOTTED: 08/20/2025
---------------	-----------------	--------------	------------------------

NORTHEAST
PRECAST

4081 S. LINCOLN AVE
VINELAND, NJ 08361
OFFICE: 866-699-2557 FAX: 856-765-9087
www.northeastprecast.com

PROJECT:
NEWBURGH SOUTH LOGISTICS CENTER

JOB NO.
25-NE1212

PIECE MARK
W266

SHEET NO.
3 OF 3
